

MEMORANDUM

DATE: June 7, 2017

TO: Brian Dissette
Bill Hunter

FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update


Current Progress:

Kalin Construction is progressing in their work to complete the new Monroe Boulevard. Kalin's crews have gotten trees planted and are continuing to complete restoration work.

The new Indian Grove Lift Station was tied in last Friday and is now online and functioning. Kalin has begun to perform final sanitary rerouting that will allow the existing pipes to be abandoned.



Construction Schedule:

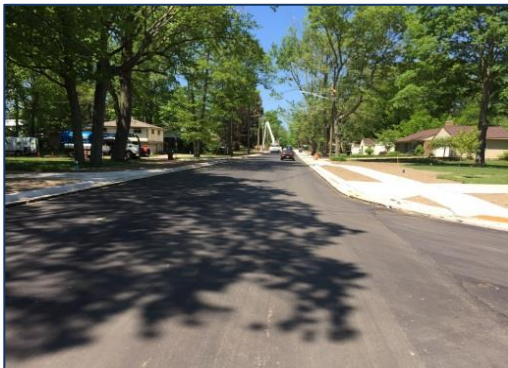

For the rest of this week, Kalin will complete sanitary rerouting work near the creek.

The crew will then begin removal of the old lift station and the old pipes that cross back and forth over the creek. This work will require the crew to get back into Monroe Boulevard near the creek. Once complete, the crew will wrap up concrete work in that area and be ready for paving.

Weekly "tailgate talks" continue to take place on Thursdays at 9:30 a.m. for anyone with project-related questions or needs. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue.
