

MEMORANDUM

DATE: October 26, 2016

TO: Brian Dissette

FROM: Corey A. Kandow, P.E.

RE: SRF #5602-01 North Shore Drive Project Update

North Shore Drive Project


Last week, Milbocker & Sons continued the installation of our new sanitary sewer and service laterals. To date, the new sanitary sewer main is installed from Dyckman Avenue to Brockway Avenue. Removal of the existing concrete sidewalk continues to be limited to isolated areas where underground utility work is taking place. As mentioned previously, the remainder of the sidewalk removal will be postponed until it is absolutely necessary for us to complete other work.

All tree removal work is complete as of this update. As fall is the best time to plant new trees, the proposed trees will be planted in September or October next year, after all other work is complete.

Over the next several weeks, sanitary sewer work on North Shore Drive will continue to move northerly. During sewer service connection work to your existing lateral, the Contractor may ask you to hold off on running water or flushing toilets until the connection is made.

Work on the new storm sewer system has also started, but has been very limited and minor. Storm sewer work will begin to pick up once the sanitary sewer and service installation is further along. Over the upcoming weeks, you can expect to see sanitary sewer, storm sewer, and even water service work taking place.

Access to North Shore Drive will continue to be restored by the close of business each day. The pulverized material will remain in place and provide a temporary gravel driving surface. Removal of the north section of North Shore

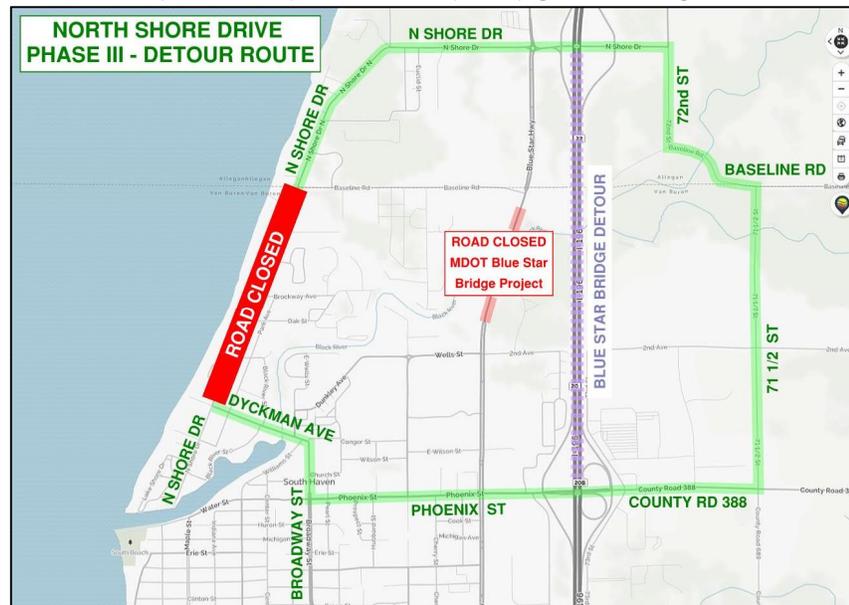

Drive (from Brockway Avenue to Baseline Road) is scheduled for early next week. This work will likely take place on either **Monday, October 31st**, or **Tuesday, November 1st**. Once removed, this portion of the project will be closed to through traffic. As mentioned above, local access will be maintained when possible during the day, and restored by means of a gravel surface by the end of each day. The proposed North Shore Drive (Phase III) detour plan is shown (left). The signed route will include North Shore Drive, 72nd Street, Baseline Road, 71 1/2 Street, County Road 388/Phoenix Street, Broadway Street, and Dyckman Avenue. North Shore Drive traffic may also choose to use MDOT's detour route on I-196 as an alternate route.

For anyone with specific project related questions, weekly on-site "tailgate talks" continue to take place on Wednesday's at 9:30 a.m. These meetings take place on the sidewalk in front of North Side Memories on Dyckman Avenue.
