

MEMORANDUM

DATE: November 16, 2016

TO: Brian Dissette
Bill Hunter

FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update

Current Progress:


The Construction crew has completed storm sewer and services to the properties along Monroe Boulevard within the Phase I limits.

The new water main has also been installed, tested and placed into service within the Phase I limits. Water services have been connected to the new water main. The new force main has been directionally bored between the lift station site and Monroe Boulevard for further extension along Monroe and Lovejoy Avenue to the project limits.

Concrete curbs and gutter work is also complete and the road crew has been working grade the roadway in preparation for asphalt paving.



Construction Schedule:

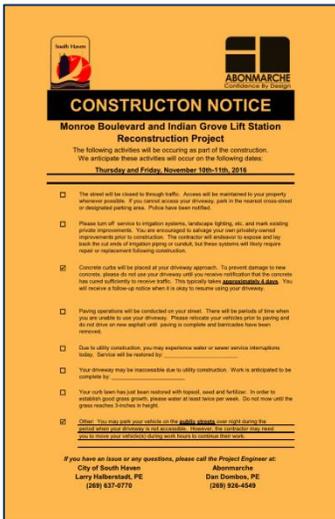

With the bulk of underground complete, roadway surfacing is the main focus of construction for the coming weeks. Keep an eye out for Construction Notices.

Asphalt paving of the first courses of asphalt is scheduled to take place Thursday, November 17th and Friday November 18th as needed. During paving, flaggers will be present to assist residents in getting to and from their homes. Keep in mind that driveways will be inaccessible for a period of time to allow asphalt to cool before it can accept traffic. Details are provided in the construction notices distributed earlier this week. Final asphalt paving will be undertaken in the spring when the entire project from Evergreen Bluff to Aylworth will be paved.

Once asphalt pavement is complete, the Concrete crew will mobilize to complete the driveway approaches. Once driveways are poured, they will be inaccessible for approximately 4-7 days, depending on the weather which controls the rate of concrete curing. Residents will be notified once the concrete has cured sufficiently to receive traffic. So, let's hope for relatively warm weather. If you have any questions, please

notify the crew or the Abonmarche inspector and they will advise you whether it will be necessary to stage a vehicle where you will be able to keep your schedule.

Weekly "tailgate talks" will continue to take place on Thursdays at 9:30 a.m. for anyone with project-related questions or needs. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue.
