

MEMORANDUM

DATE: September 14, 2016

TO: Brian Dissette

FROM: Corey A. Kandow, P.E.

RE: SRF #5602-01 Project Updates


North Shore Drive Project

Construction on Dyckman Avenue continues to draw closer and closer to an end. This week the contractor installed all of the underground utilities, and is currently finishing up the underground work within the North Shore Drive/Dyckman intersection. The detour route signage for both northbound and southbound North Shore Drive, have been adjusted to more clearly define the route. Local

business open signs have also been installed this week. Our first "tailgate talk" took place today and had a great turnout. These on-site informal meeting will continue weekly on Wednesday's at 9:30 a.m. Early/mid next week, the Contractor is expected to start aggregate base and concrete work flatwork on Dyckman Avenue. Currently paving of Dyckman Avenue is scheduled for Thursday (9/22/16) and/or Saturday (9/24/16).



Once Dyckman is paved, striped, and reopened to traffic, construction will shift onto North Shore Drive and proceed northerly. Traffic control signage for the south half of North Shore Drive (Dyckman to Brockway) is scheduled to be installed on Monday, September 26, 2016. During this portion of the work, North Shore Drive traffic will use Dyckman Avenue, Park Avenue, and Brockway Avenue as shown on the attached map. On Tuesday, September 27, 2016, Millbocker will begin milling/pulverizing the surface of North Shore Drive. This pulverized material will remain in place and provide a gravel type driving surface for residents within the construction limits.

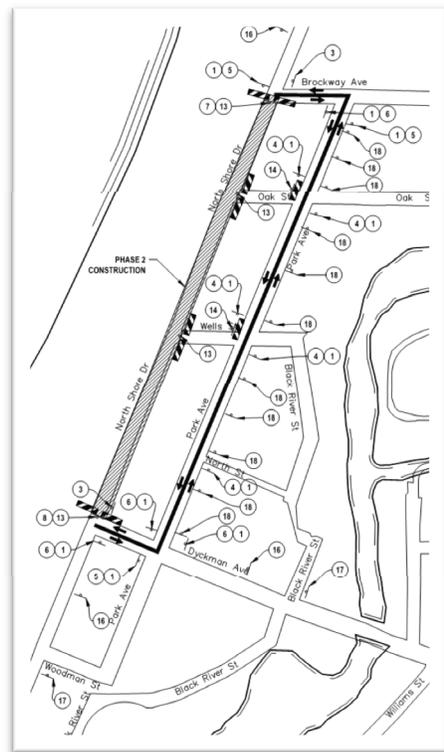

Dunkley & Black River Street Project

Milbocker & Son's has indicated that they anticipate starting construction around January 9th, 2017 on the Dunkley & Black River Street project. Davis Construction has indicated that they plan to begin work on the Waste Water Treatment Plant (WWTP) on September 19, 2016.

Monroe Boulevard & Indian Grove Lift Station Project

Kalin Construction plans to start the Monroe Boulevard and Indian Grove Lift Station the week of October 10th, 2016.

