City of South Haven

Department of Public Works

DPW Building • 1199 8th Ave. • South Haven, Michigan 49090
Telephone (269) 637-0737 • Fax (269) 637-4778

Dyckman Avenue Bascule Bridge Rehabilitation

Progress Report – Week 10

The following work was performed during the week of December 15-19, 2014:

- Completed scour repairs at bridge piers
- Completed repairs to grouted rip-rap on river banks
- Installed and grouted rip-rap at new storm sewer outlet
- One coat of primer applied to structural steel
- Installed new floor beams and steel for road curbs

It is anticipated that the following work items will be completed in the coming weeks:

- Complete structural steel erection
- Complete painting of all steel on center span
- Begin electric work and hydraulic machinery installation

Grouted Rip-Rap Repairs

New Grouted Rip-Rap and Storm Sewer Outlet

Installing Steel Roadway Curb

New Floor Beams from Below

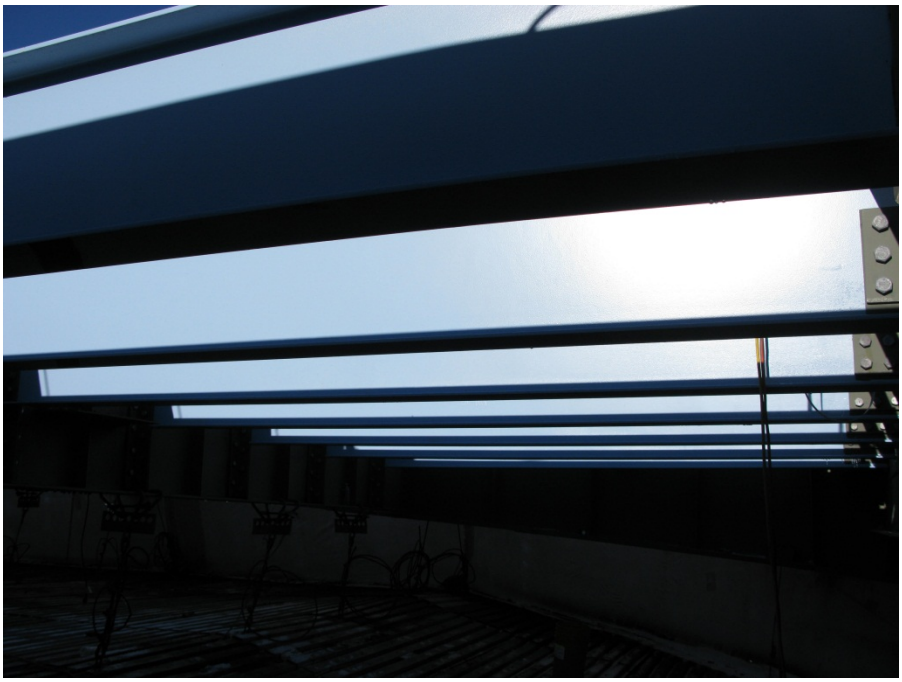

New Floor Beams from Above
